


Orig Dur	Rem Dur	%	Early Start	Early Finish	Total Float	JAN																						
						5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23				
						0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16	0, 8, 16		

BU Boiler Unit

BOIL

William F. Simon - Boilermaker/Mech Supervisor

8	1	88	07JAN00 16:00A	08JAN00 06:59	83
8	8	0	08JAN00 07:00	08JAN00 15:59	111
8	8	0	08JAN00 07:00	08JAN00 15:59	83
8	8	0	08JAN00 16:00	10JAN00 06:59	111
12	12	0	08JAN00 16:00	10JAN00 11:59	131
4	4	0	08JAN00 16:00	08JAN00 20:59	83
16	16	0	10JAN00 12:00	11JAN00 11:59	131
16	16	0	11JAN00 12:00	12JAN00 11:59	107

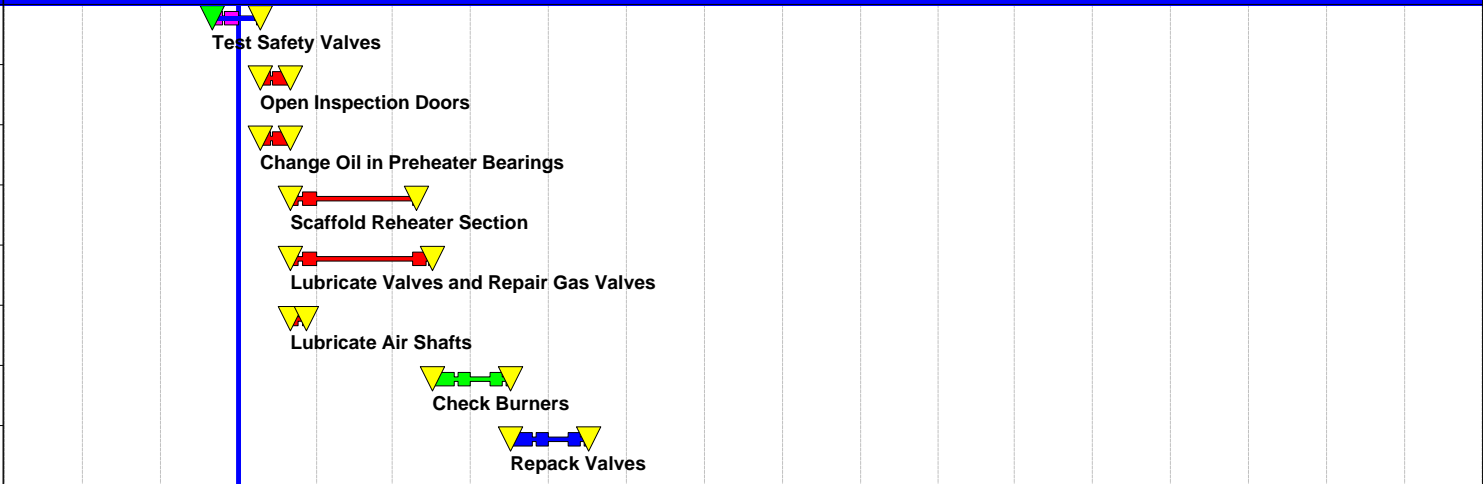

OPER

Kathleen M. Black - Operations Manager

8	8	0	14JAN00 12:00	14JAN00 20:59	83
---	---	---	------------------	------------------	----



PIPE

Michael S. Reese - Pipefitter Supervisor


36	36	0	08JAN00 07:00	11JAN00 11:59	107
----	----	---	------------------	------------------	-----



WELD

John R. Daly - Welder Superintendent

24	24	0	08JAN00 21:00	11JAN00 11:59	83
40	40	0	10JAN00 07:00	12JAN00 15:59	111
12	12	0	11JAN00 12:00	12JAN00 06:59	111
48	48	0	11JAN00 12:00	14JAN00 11:59	83
8	8	0	12JAN00 12:00	12JAN00 20:59	107

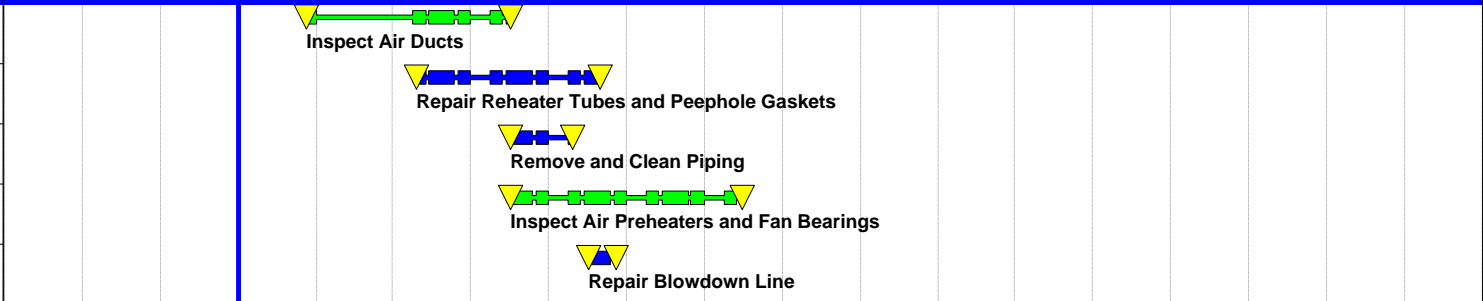


TU Turbine Generator


BOIL

William F. Simon - Boilermaker/Mech Supervisor

8	1	88	07JAN96 16:00A	08JAN00 06:59	89
8	0	100	07JAN00 06:00A	07JAN00 18:59A	



Project Start 05JAN00 00:00
 Project Finish 22JAN00 12:59
 Data Date 08JAN00 00:00
 Run Date 25MAR99 21:00



OUTG

Northeast Utilities Co.
 Demonstration Outage Project
 Grouped by Subproj & Responsibility

