


Activity ID	Orig Dur	Rem Dur	%	Early Start	Early Finish	E J F M A M J J A S O N D J F M A M J J A S O N D J F M A M J																											
-------------	----------	---------	---	-------------	--------------	---	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

<b>Clinical Research and Development</b>						<b>CLIN</b>																											
<b>Process Scale-up and Stability</b>						<b>SCALE</b>																											
<b>Pharmacy R&amp;D</b>						<b>PHR&amp;D</b>																											
A0005	180	63	65	03JAN99A	05JUL99																												
A0015	80	50	38	04APR99A	24AUG99																												
A0025	100	100	0	25AUG99	04DEC99																												

<b>Phase 3 Clinical Development</b>						<b>PH3</b>																											
<b>Medical</b>						<b>MED</b>																											
A1002	30	0	100	04JAN99A	15FEB99A																												
A1005	37	0	100	07JAN99A	17MAR99A																												
A1010	10	0	100	16FEB99A	02MAR99A																												
A1012	30	0	100	03MAR99A	13APR99A																												
A1015	35	4	89	18MAR99A	05MAY99																												
A1030	134	80	40	28JAN99A	10AUG99																												
A1032	109	70	36	28MAR99A	25AUG99																												
A1033	119	119	0	16JUN99	14OCT99																												
A1056	84	84	0	11AUG99	03NOV99																												
A1082	60	60	0	20DEC99	19FEB00																												
A2002	20	20	0	01JUN99*	20JUN99																												
A2005	30	30	0	06JUN99	06JUL99																												
A2010	10	10	0	21JUN99	30JUN99																												
A2012	30	30	0	01JUL99	31JUL99																												
A2015	35	35	0	07JUL99	10AUG99																												
A2030	134	134	0	26AUG99	10JAN00																												
A2032	109	109	0	06OCT99	25JAN00																												
A2033	119	119	0	16OCT99	14FEB00																												
A2056	84	84	0	11DEC99	06MAR00																												
A2082	60	60	0	21APR00	20JUN00																												

Project Start: 03JAN99 Project Finish: 09NOV00 Data Date: 02MAY99 Run Date: 24MAR99		CLIN Pharmaceutical Laboratories, Inc. Clinical Research and Development Grouped by Responsibility And Phase	Sheet 1 of 3
--	--	---	--------------

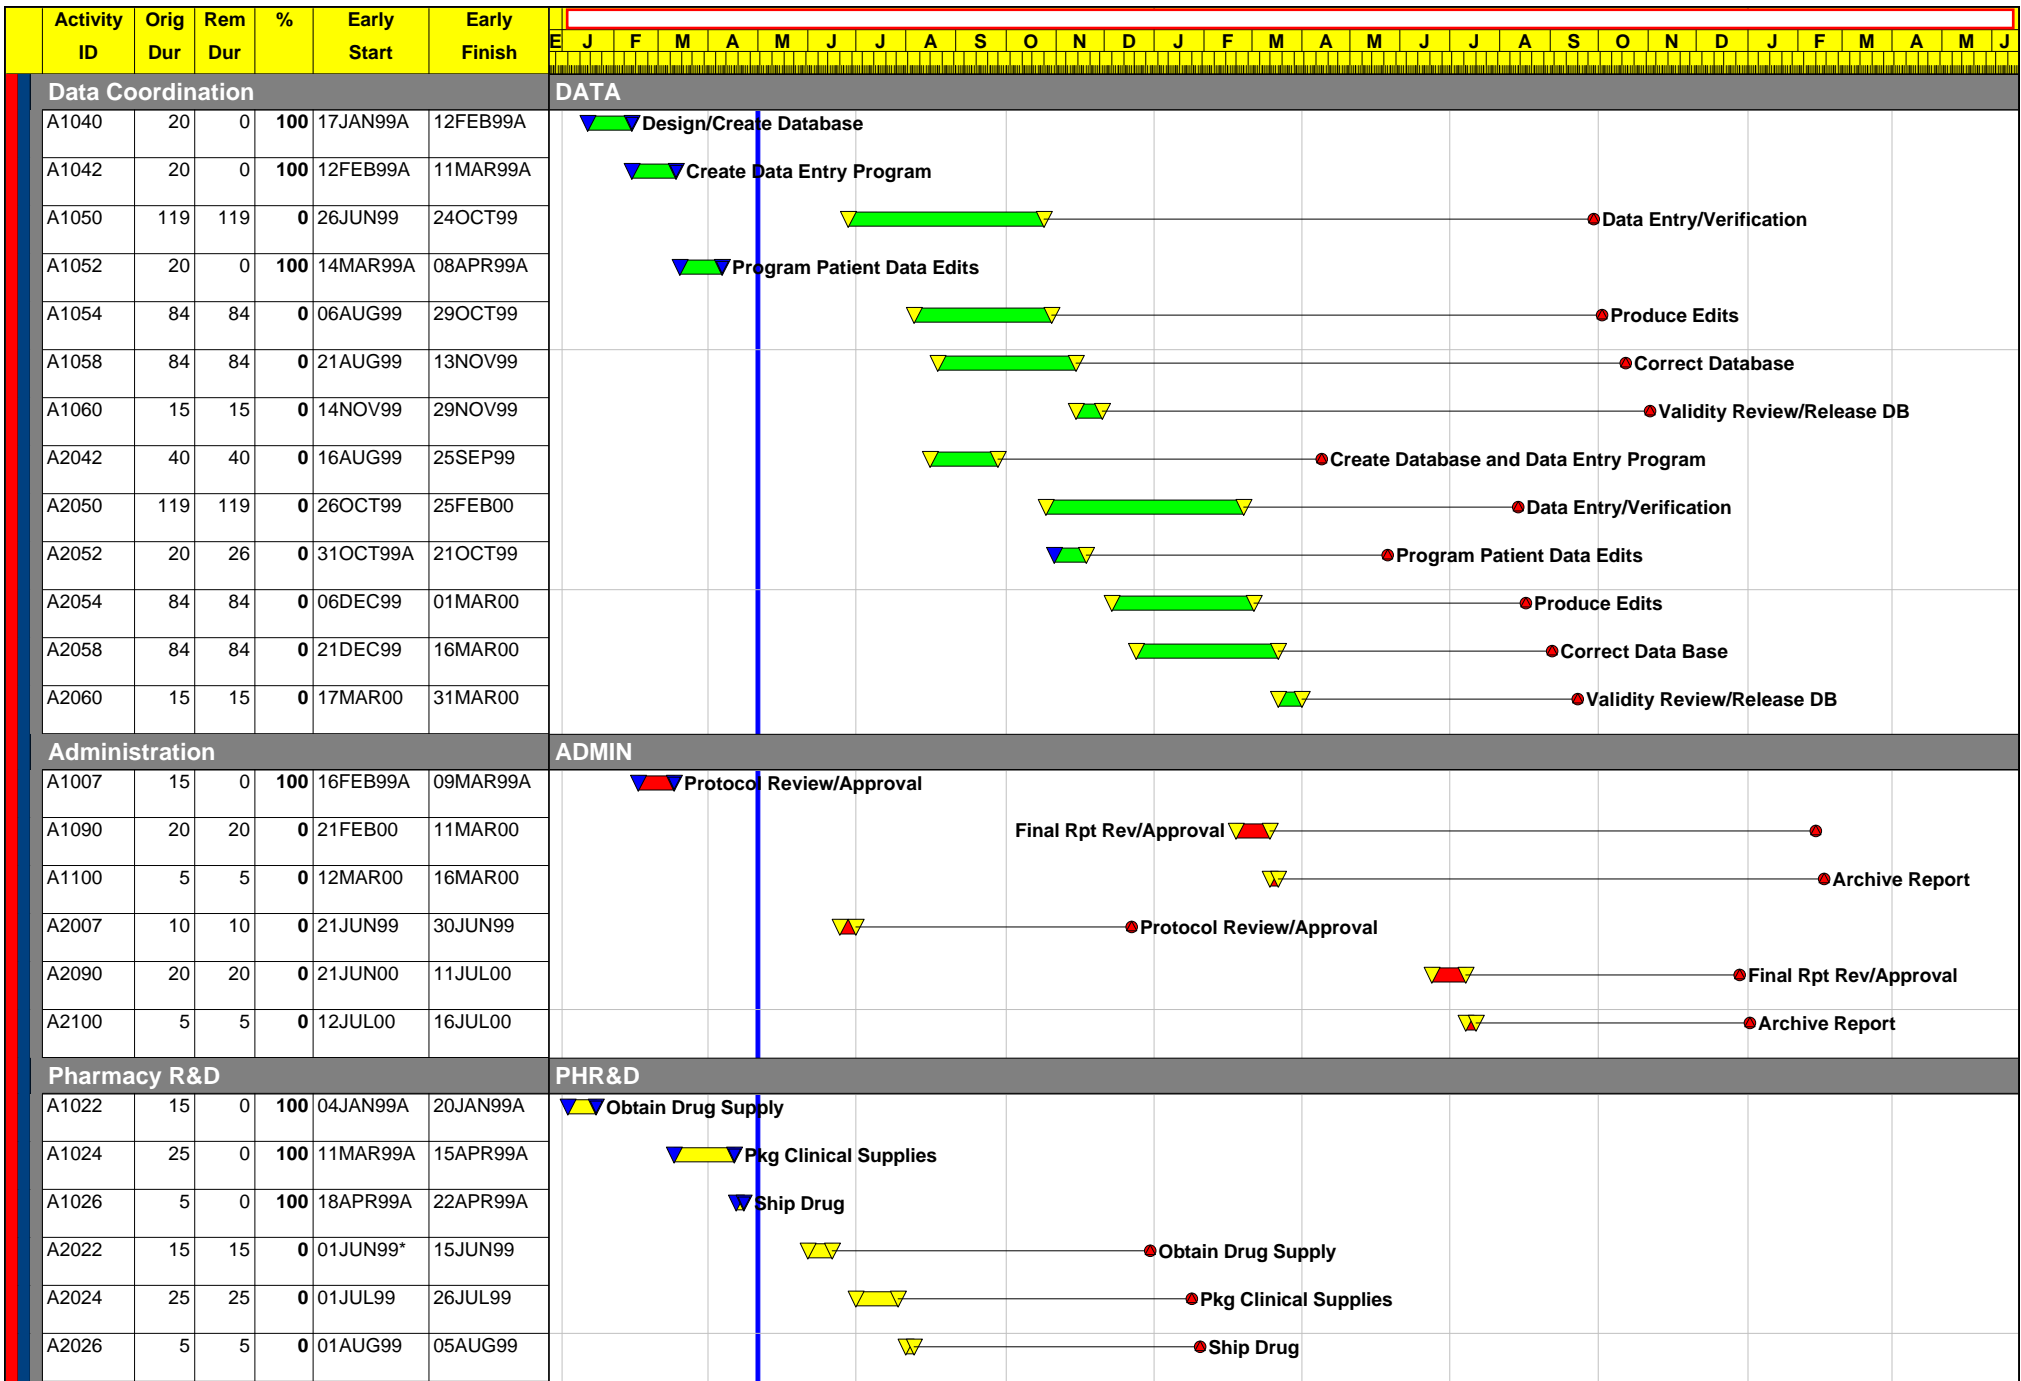


Project Start	03JAN99		Early Bar
Project Finish	09NOV00		Float Bar
Data Date	02MAY99		Progress Bar
Run Date	24MAR99		Critical Activity

© Primavera Systems, Inc.

CLIN

Pharmaceutical Laboratories, Inc.  
Clinical Research and Development  
Grouped by Responsibility And Phase

Sheet 2 of 3

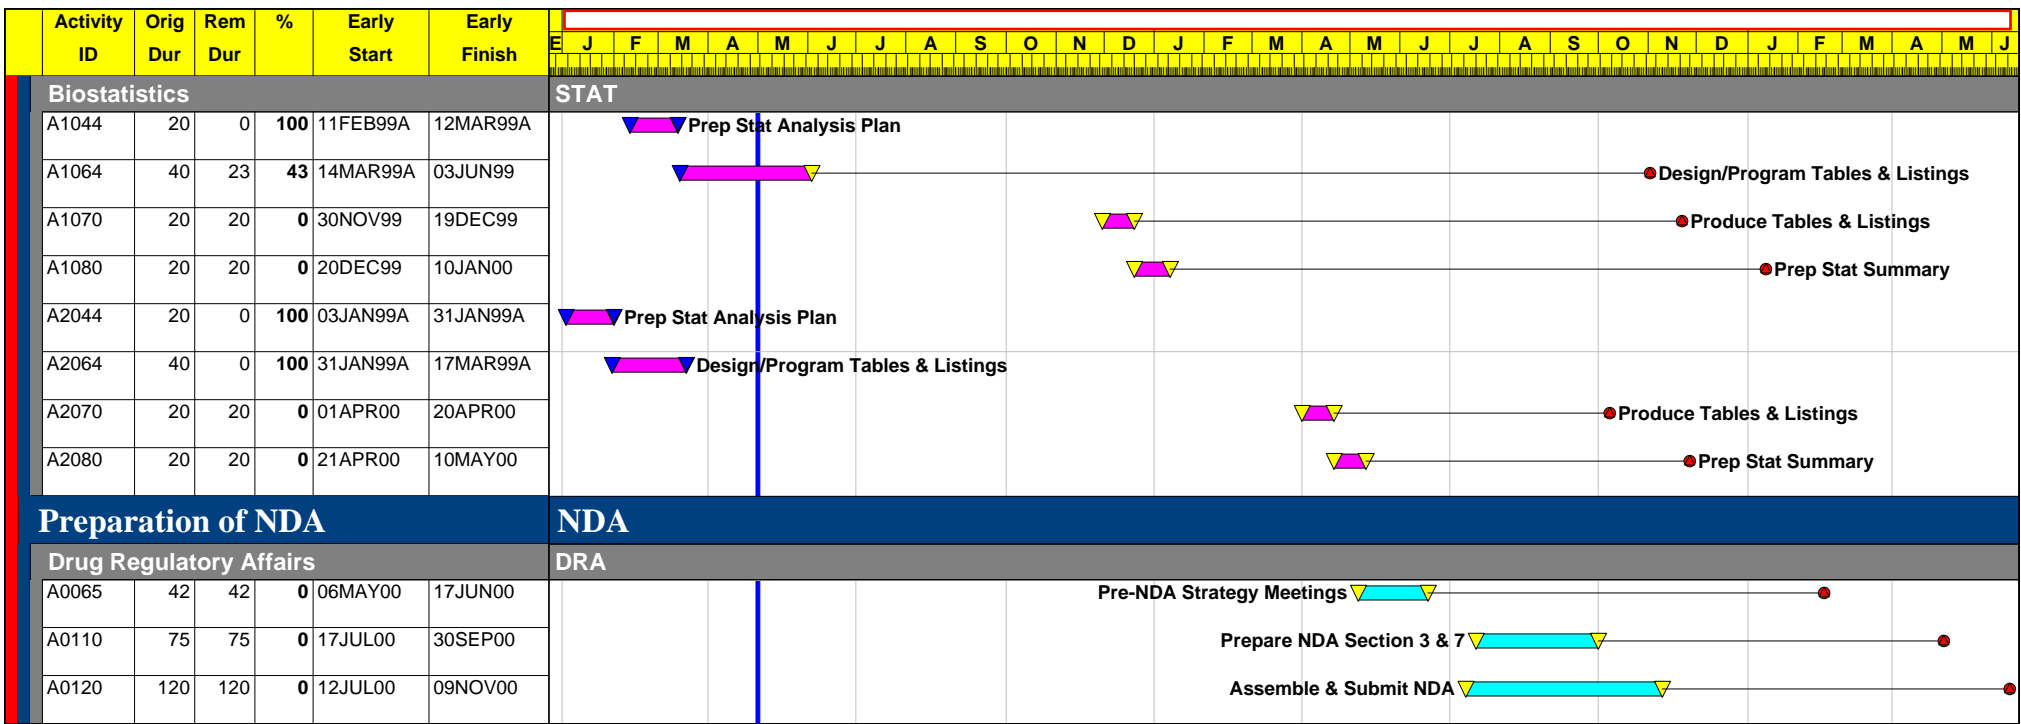

Project Start	03JAN99		Early Bar
Project Finish	09NOV00		Float Bar
Data Date	02MAY99		Progress Bar
Run Date	24MAR99		Critical Activity

CLIN

Pharmaceutical Laboratories, Inc.  
 Clinical Research and Development  
 Grouped by Responsibility And Phase
